



Street Rehabilitation Project Update



Tom Koper, P.E.
Acting Public Works Director
January 15, 2020


Sixth Street and Yorba Street Waterline Replacement and Pavement Rehabilitation Project



PHASE 2
Daytime Pipeline Construction
Monday - Friday 7:00 AM - 3:30 PM
Construction from mid-February to May 2020

PHASE 1
Nighttime Pipeline Construction
Sunday Night - Friday Morning 9:00 PM - 4:00 AM
Construction from mid-January to mid-February 2020

Hayden and Howe Street Waterline Replacement Project

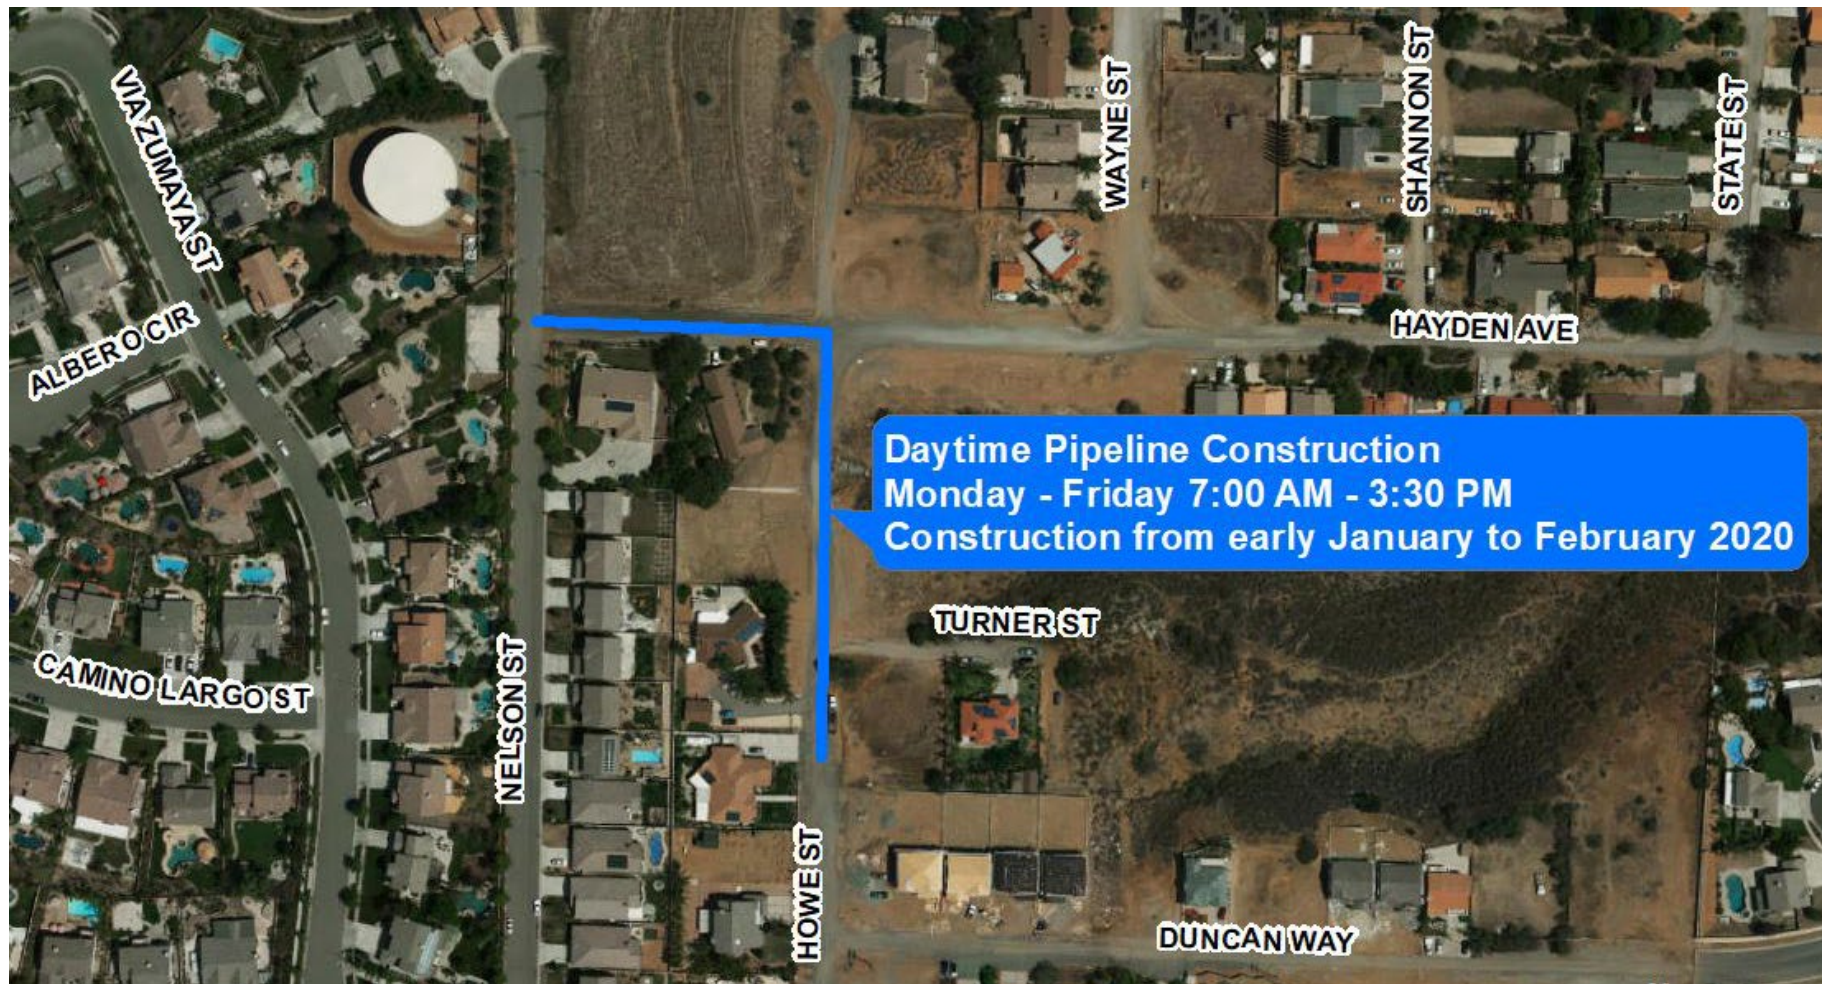


Daytime Pipeline Construction
Monday - Friday 7:00 AM - 3:30 PM
Construction from early January to February 2020

Street Pavement Maintenance and Rehabilitation Project

Street Pavement Maintenance and Rehabilitation Project

Work Completed:

- ❑ **Foothill Boulevard:** Paving complete
- ❑ **California Avenue:** Paving complete, and striping 95% complete
- ❑ **Border Avenue and Via Del Rio:** Paving complete, and striping 90% complete
- ❑ **Magnolia Avenue:** Paving and striping complete
- ❑ **Parkview Drive:** Paving complete
- ❑ **Sampson Avenue:** Paving and striping complete
- ❑ **Residential neighborhoods in Areas A, B, C, and D:** Paving and preliminary striping complete. However, asphalt rubberized aggregate membrane (ARAM) and slurry seal are not complete.

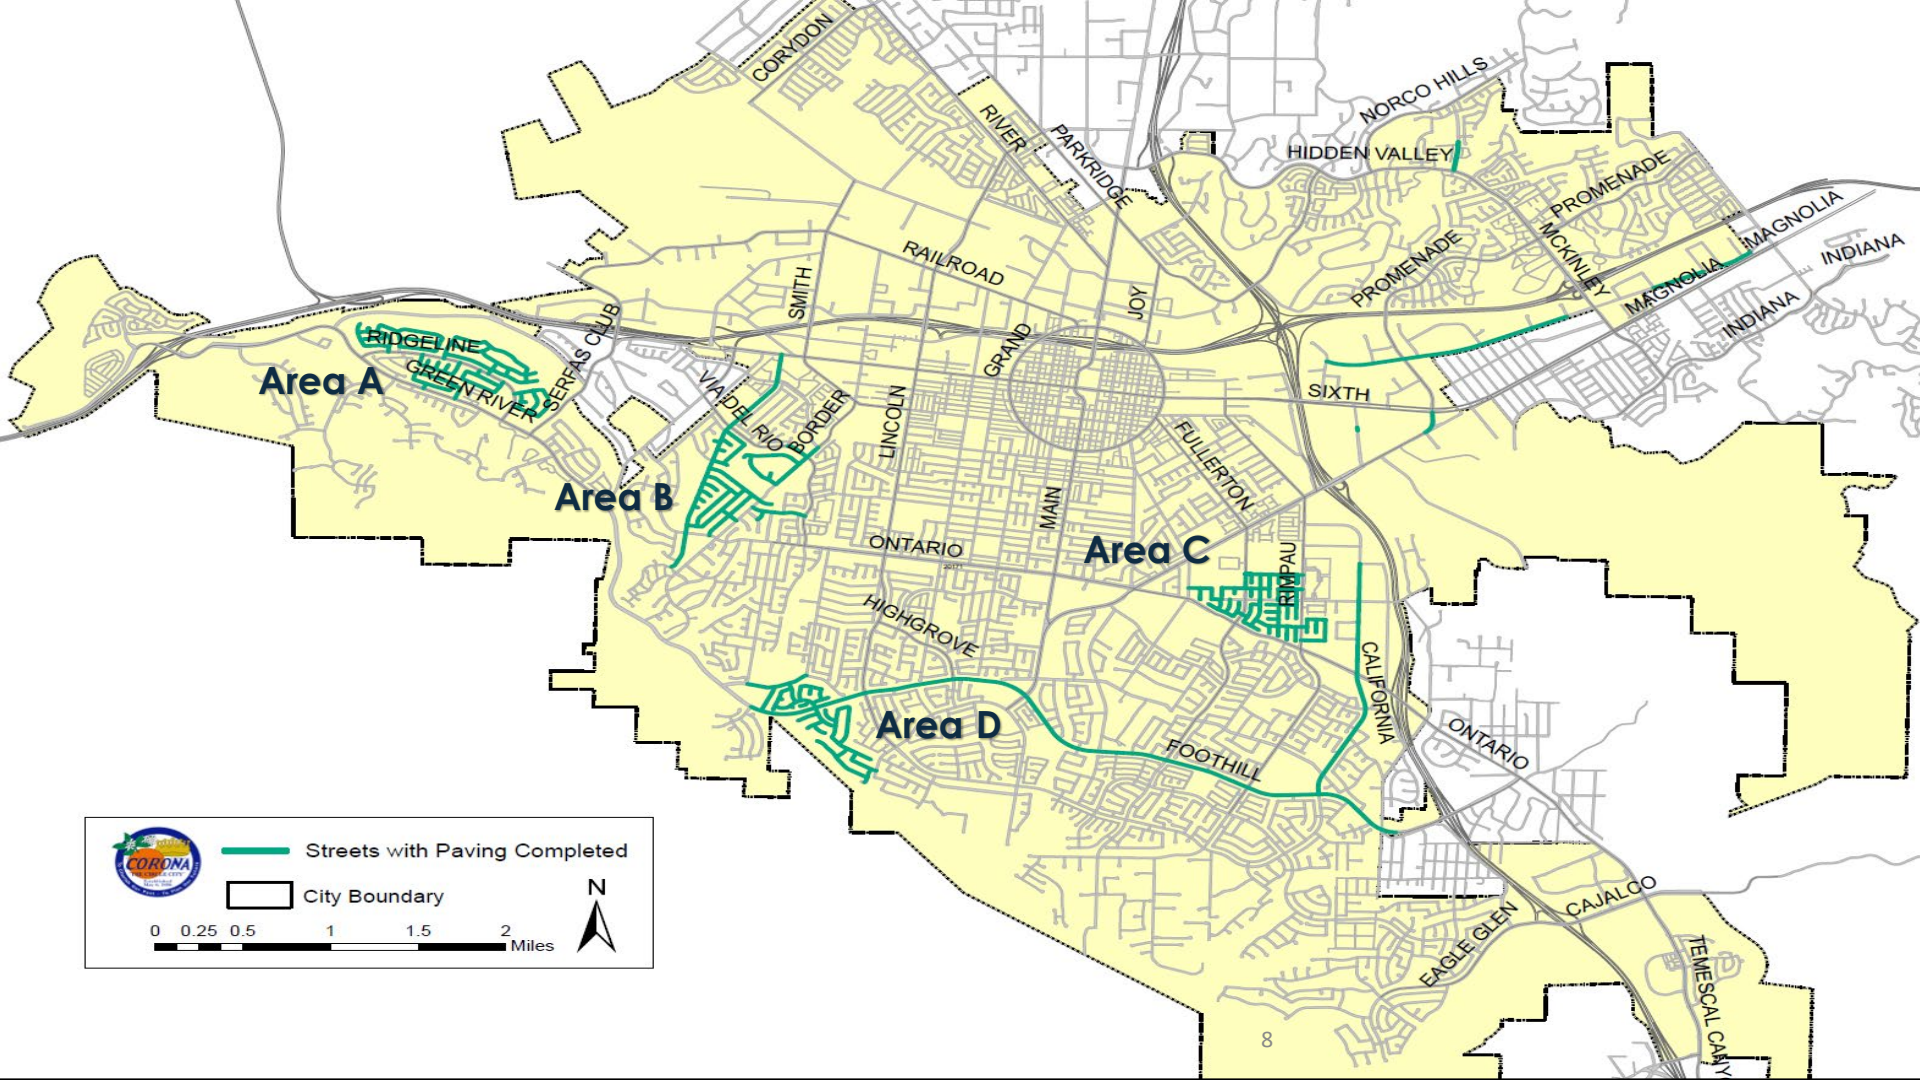


Streets with Paving Completed



City Boundary

0 0.25 0.5 1 1.5 2 Miles



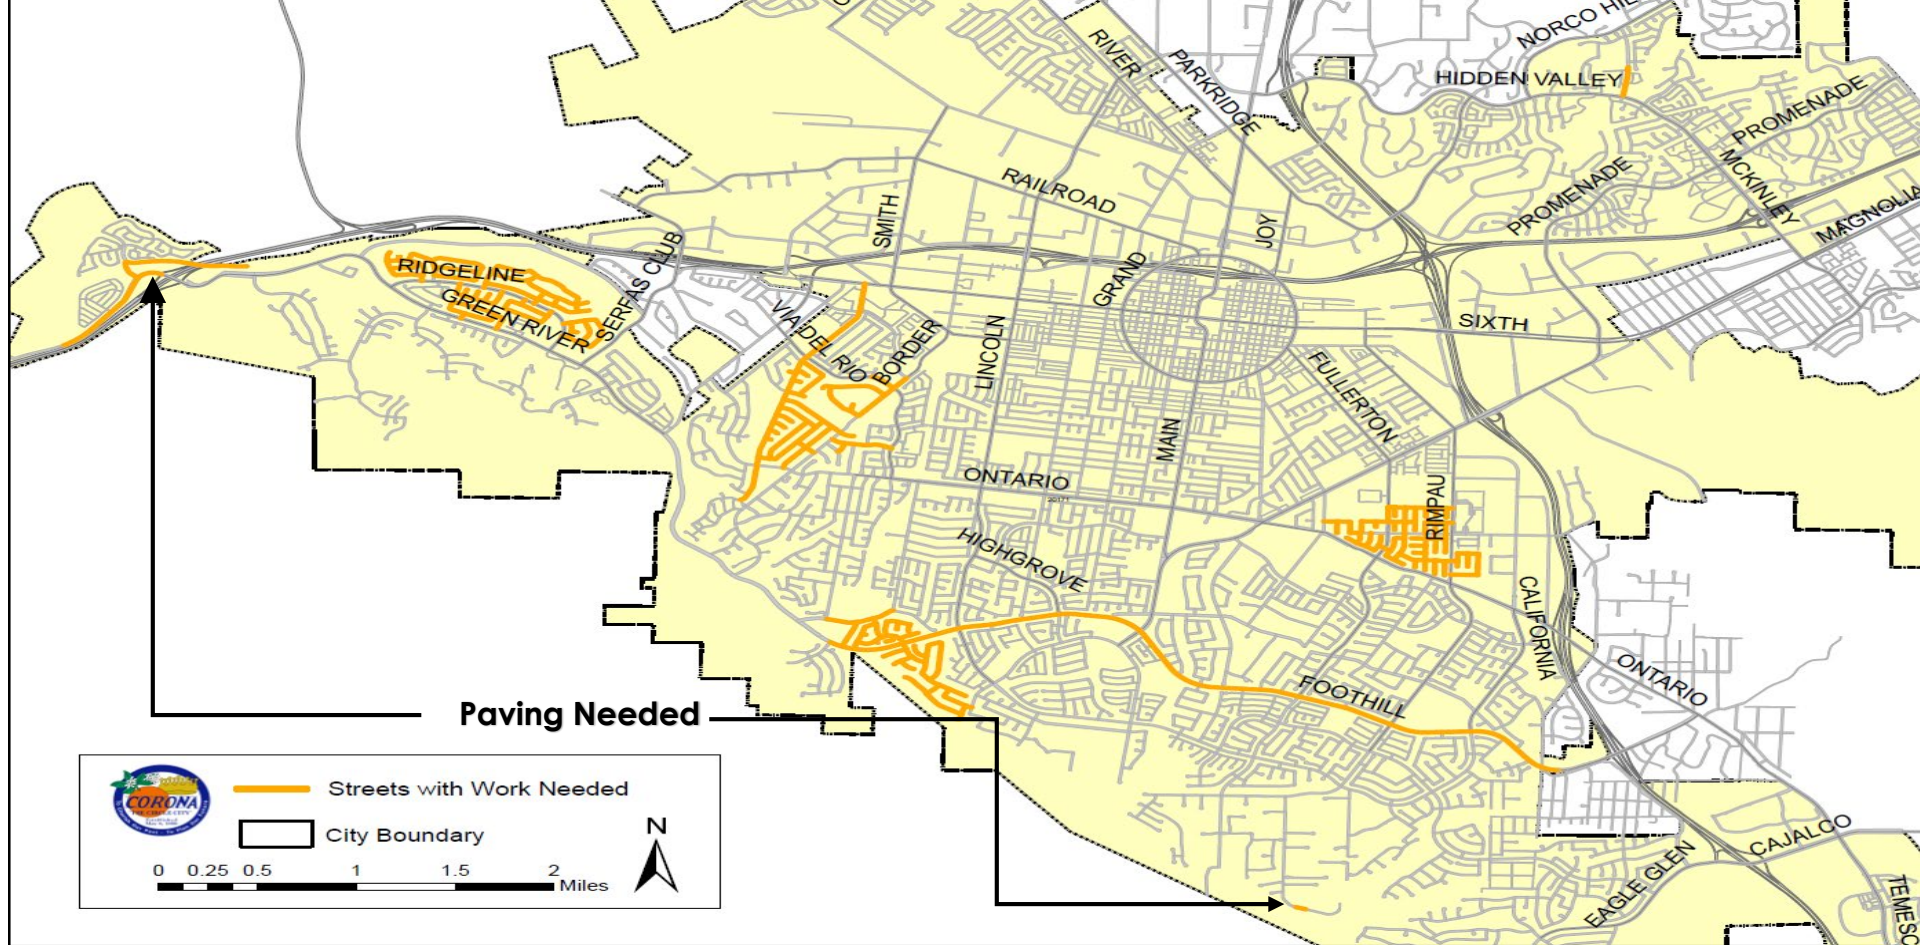

Paving Needed to be Completed:

Green River Road, Prado Road, Crestridge Drive, and Hidden Springs Drive

ADA Ramps

Work Completed:

Upgraded 34 curb ramps to ADA compliance



Before



After



Location Map: ADA Ramps Installed

QUESTIONS?



Public Works 951-736-2266



www.CoronaCA.gov





www.CoronaCA.gov

